


George Street North Pedestrianisation

Construction Update | December 2024

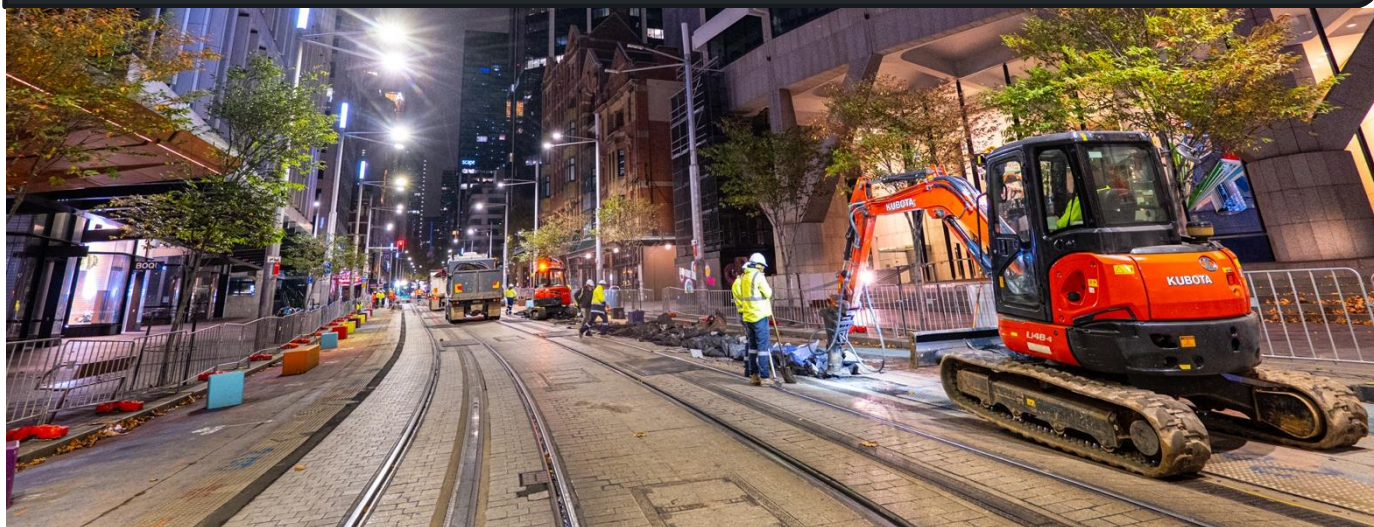

Pictured: 17-18 May 2024 construction work on George Street.

Sydney Civil are working to improve George Street between Hunter Street and Essex Street, Sydney as well as selected side streets as part of the wider George Street North Pedestrianisation project. We will install new granite paving, upgrade the stormwater drainage, planting new trees and installing street furniture to make the pedestrian boulevard on George Street more accessible to people.

Work completed to date

Since May 2024, we have completed upgrades at the following locations:

- Bond Street to Curtin PI (east)
- Hunter Street to Jamison Street (west)
- Grosvenor Street to Essex Street (west)
- Bridge Street to Essex Street (east)

Thank you to everyone for their patience and cooperation during construction work.

Three month lookahead – January to March 2025

- Margaret Street between George Street and Wynyard Lane.
- George Street - Curtin PI to Hunter Street (east).

We will continue to notify businesses and residents in advance of upcoming work.

From January 2025: Margaret Street between George Street and Wynyard Lane.

- Removal of concrete blocks, set up fences at opposite side to mirror concrete barriers corridor and set up water barriers along the footpath edge.
- Street improvements including footpath widening and upgrade, underground utilities/services adjustments, drainage and road improvements, lighting and landscaping works.

From January 2025: Curtin PI to Hunter Street (east)

- Removal of concrete blocks, set up fences at opposite side to mirror concrete barriers corridor and set up water barriers along the footpath edge.
- Excavation of 1m asphalt strip along the Light Rail track prior concrete barriers installation (minor noise expected).

- Street improvements including footpath widening and upgrade, underground utilities/services adjustments, drainage and road improvements, lighting and landscaping works.

Temporary traffic changes

Throughout our work there are temporary parking, access and traffic changes on George Street and side streets to create safe work environment for our workers and the community. Traffic control and signage will be in place. Please follow the direction of traffic controllers. Traffic changes across the next three months includes:

- Temporary parking removal (in sections)
- Temporary footpath closures with temporary detours
- Temporary parking lane changes

Construction progress photos



Areas completed and opened to the public in 2024 along George Street

Year-end break from construction

From Saturday 21 December to Monday 13 January our project site will be closed over the holiday period. We wish you and your loved ones a safe and happy holiday season. We look forward to a productive 2025 working with the George Street community.

Standard construction hours Contact us

Construction work will be carried out generally during the day between **7:30am and 5:30pm Monday to Friday** and **7:30am to 3:30pm on Saturdays**. We aim to minimise night works as much as possible, however working next to the light rail environment and TfNSW controlled roads, will require night work. We will provide notification in advance to nearby residents and businesses.

Contact us

If you have any questions or would like more information, please contact our community team.

Email us - community@sydneycivil.com

Scan the QR code to access Sydney Civil's information webpage for more details on the project.

Subscribe to receive our weekly email updates on construction progress. Register online or email us.

